

No.

3 / AUT 3

temporary certificate

## CERTIFICATE OF JUMPING HILL CERTIFICAT DE CONFORMITE SCHANZENPROFILBESTÄTIGUNG

Date of issue

22.01.2018

Valid till

31.12.2018

Établi le Ausgestellt am Valable jusq` au

Gültig bis

Place:

Seefeld

Name:

Toni-Seelos-Schanze

HS =


109 m

h/n =

0,555

Vo =

24,79 m/s

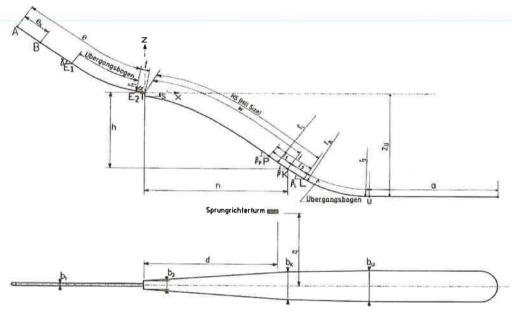

е	=	91,36 <b>m</b>		I <sub>1</sub>
es	=	18,21 <b>m</b>	33 gates	$I_2$
t	=	5,77 <b>m</b>		а
γ	=	34,00°		$\beta_{p}$
α	=	11,50°		β
$\Gamma_1$	=	95,20 <b>m</b>		$\beta_{L}$
h	=	48,29 <b>m</b>		$\mathbf{r}_{L}$
n	=	86,96 <b>m</b>		Γ <sub>2L</sub>
S	=	2,46 <b>m</b>		r <sub>2</sub>

l <sub>1</sub>	=	10,04 <b>m</b>	z <sub>U</sub>	=	74,95 <b>m</b>
$I_2$	=	9,93 <b>m</b>	Р	=	88,96 <b>m</b>
а	=	92,00 <b>m</b>	K	=	99,00 <b>m</b>
$\beta_{p}$	=	35,80 °	L	=	108,89 <b>m</b>
	=	33,30 °	b <sub>1</sub>	=	2,61 <b>m</b>
$\beta_{L}$	=	31,00 °	b <sub>K</sub>	=	19,55 <b>m</b>
$\mathbf{r}_{L}$	=	230,00 <b>m</b>	bυ	=	21,50 <b>m</b>
r <sub>2L</sub>	=	200,00 <b>m</b>	d	=	79,63 <b>m</b>
ľ2	=	110,00 <b>m</b>	q	=	19,85 <b>m</b>

## **Remarks / Bemerkungen**

- 1. inspection by Hans-Martin Renn (15th October 2016) as part of TD-seminar 2016 in Seefeld
- 2. the remarks of the inspection-report must be observed and fulfilled for the validity of certification.
- 3. worked out mistakes of the inspection report see documentation (17th January 2018)
- 4. for fulfilling the (ICR/IWO) standards of the jumpinghill, the owner is responsible during training and competition.
- 5. during training and competition the temporary guard-rail-solution of Seefeld must be installed (see remark no.5 of the report)

JUMPING HILL APPROVED BY THE FIS
TREMPLIN HOMOLOGUE PAR LA FIS
DURCH DIE FIS GENEHMIGTE SPRUNGSCHANZE

SUB-COMMITTEE FOR JUMPING HILLS

**CHAIRMAN:** 

Hans-Martin Renn

FÉDÉRATION INTERNATIONALE DE SKI INTERNATIONAL SKI FEDERATION INTERNATIONALER SKI VERBAND
